


Build ID: MTC_7K_10s_1777049033 | Machine: DMP 350 Triple H - LMP126 | Date: 2026-04-24 16:44:15 UTC

NEEDS REVIEW

3D Build Viewer

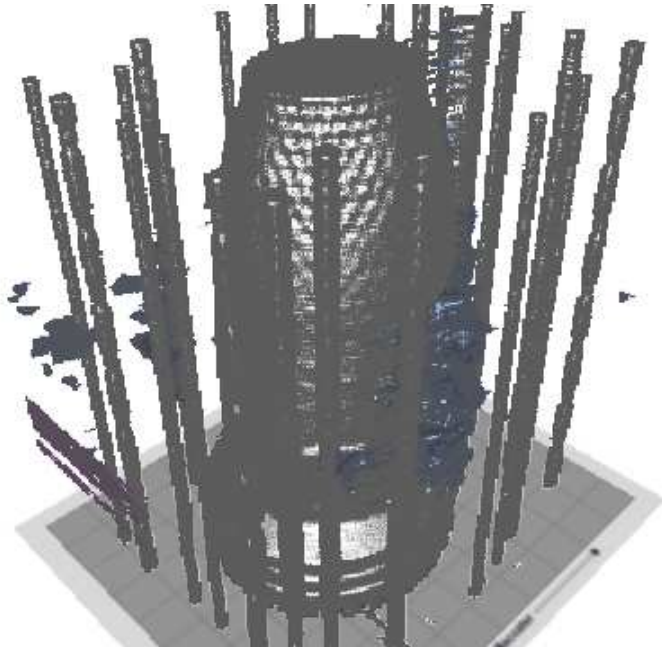

3D view at default camera angle (captured at report creation time)

Build Summary

Machine	
Machine Name	DMP LMP126
Machine ID	DMP 350 Triple H - LMP126
Build Job	
Build ID	MTC_7K_10s_1777049033
Layers Printed	7076
Build Height (mm)	424.56
Job Start	2026-04-24 16:44:15 UTC
Job Finish	2026-04-26 08:09:39 UTC
Duration	1 day 15 hours 25 minutes 16 seconds
Status	Completed
Critical Anomalies	770

Total Anomalies

2814

Critical

770

Layers Printed


7076

Anomalies Summary (Total: 2814)


Anomaly	Severity	Volume (mm³)	Count
Recoater Line	Critical	0.00	0
Short Feed	Critical	76300.51	713
Warpage	Critical	187.89	57
Recoater Hopping	Critical	0.00	0
Recoater Line	Moderate	2.65	1
Short Feed	Moderate	150509.14	782
Warpage	Moderate	3350.87	1259
Recoater Hopping	Moderate	2709.50	2

Images in this report have been downscaled for local storage optimisation. Full-resolution RAW data is available on the AMVero On-Prem server.

Layer: 1

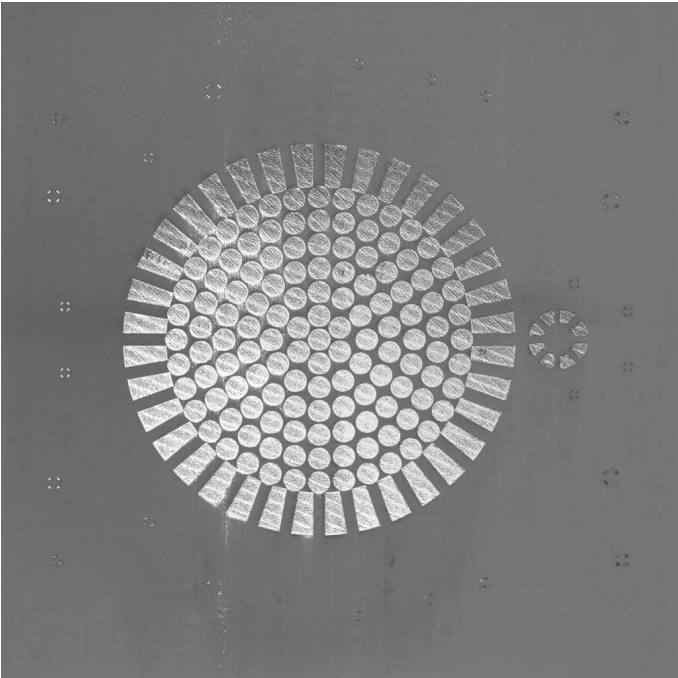

Post Recoating

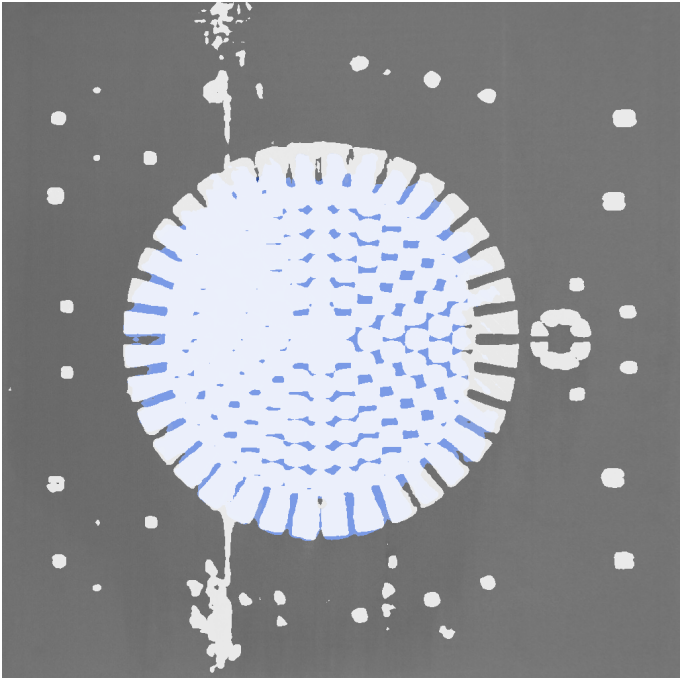

Post Exposure with Anomalies

Anomaly Details

Type: Short Feed Area: 27358.78 mm² Layer Height: 0.06 mm **Severity: Critical**

Images have been downscaled for reporting purposes.
